



Type of Product
ZGS-H-225/24940-600/347


Serial No: JM2307043
Drawing No:ZGS-H-225-230720-01

1 Description				
Name of Product		Three-phase Distribution Pad Mount Transformer		
Type of Product		ZGS-H-225/24940-600/347		
Serial No.		JM2307043		
Drawing No.		ZGS-H-225-230720-01		
2 Technical Specification				
Power Rating		225kVA	Cooling Type	ONAN
Rated Voltage		24.94/0.6kV	Number of Phases	3 Phases
Rated Current		5.209/216.5A	Rated Frequency	60 Hz
Vector Group		YNyn0		
Basic Insulation Level	HV	LI/AC		
	LV	LI/AC		
3 Applicable standards				
ANSI/IEEE C57.12.00 General Requirements for Liquid-Immersed Distribution, Power and Regulating Transformers ANSI/IEEE C57.12.90 Test Code for Liquid-Immersed Distribution, Power and Regulating Transformers ANSI/IEEE C57.12.80 Standard Terminology for Power and Distribution Transformers ANSI/IEEE C57.100 IEEE Standard Test Procedure for Thermal Evaluation of Liquid-Immersed Distribution and Power Transformers ANSI/IEEE C57.136 IEEE Guide For Sound Level Abatement & Determination For Liquid-Immersed Power Transformers & Shunt Reactors Rated Over 500 KVA ASTM D 6871 Standard Specification for Natural (Mineral/Vegetable Oil) Ester Fluids Used inElectrical Apparatus AWS American Welding Society NEMA National Electrical Manufacturers Association NFPA TO National Fire Protection Association National Electrical Code SSPC The Society for Protective Coatings Paint Application Specification NO. 2 CSA C227.4:21 National Standard of Canada				

1 、 Specification										
Rated Capacity (KVA)	225	Product Type	ZGS-H-225		60HZ	Factory Serial No.	JM2307043			
3Voltage Combination	HV(kV)	24.94	Current	HV (A)	5.209	Angular displacement	YNyn0			
	LV(kV)	0.6		LV(A)	216.5					
2 、 Measurement of voltage ratio										
Tapping Position	HV and LVThe Voltage Value of the Test	HV (V)	LV (V)	HV/LV (%)						
				AB/ab		BC/bc		AC/ca		
1	The Grade and Accuracy:QJ3 5A Grade 0.2	26187	600	0.06		0.08		0.05		
2		0.10		0.12		0.09				
3		0.14		0.16		0.13				
4		0.12		0.14		0.11				
5		0.10		0.13		0.09				
3 、 Measurement of winding resistance (Routine)										
Tapping Position	Winding Resistance Measurement	HV (Ω)						LV(Ω)		
		H0H1A	H0H2A	H0H3A	H1AH1B	H2AH2B	H3AH3B	xox1	0.006986	
1		18.07	17.94	18.01	36.01	35.95	36.08	xox2	0.006909	
2		17.60	17.47	17.53	35.07	35.00	35.14	xox3	0.006798	
3		17.13	17.00	17.06	34.12	34.06	34.19	x1x2	0.01364	
4		16.66	16.52	16.58	33.18	33.12	33.24	x2x3	0.01347	
5		16.17	16.04	16.10	32.21	32.13	32.27	x3x1	0.01355	
The Meter NO. and Grade ofAccuracy		HCR3102A Grade 0.2		Temperature		28 °C		Humidity		100%
4 、 No-load loss and no-load current test.										
Test Items		No-Load Loss at 100% rated voltage W				No-Load Current %				
Measured Value		479				0.32				
5 、 Load loss and Short circuit test.										
Test Items	Load Loss at 8 5°C and rated voltage W			Total Loss W		Short Circuit Impedance at 8 5°C				
Measured Value	2940			3419		4.40				

6 、 Applied voltage test				
Power Frequency withstand Voltage Test				
Test Time	60 S			
The Test Voltage(kV)	HV 40 /LV10			
7 、 Induced Over Voltage Withstand Test				
Induced Over Voltage Withstand Test(kV)	1.2 (rms) for L.V. bushing			
8 、 Insulation Resistance test				
location	Insulation Resistance(M Ω) at 28℃ R60			
HV-LV	>2500			
HV-E	>2500			
LV-E	>2500			
9 、 Other Information.				
The Active Part's Weight of Lifting	The Weight of Insulation Oil	Total Weight	The Temperature Rise of the Oil	Oil Pressure
888kg	1000kg	2510kg	<65K	45KV
10 、 Leakage test (Routine)				
Test method	Applied pressure (kPa)	Duration (h)	Residual pressure (kPa)	Result
The static pressure method	35	12	35	No leakage and no damage
11 、 Outer inspection				
The nameplate, sign, earthing terminal, mark of terminal meets the requirement. There is no evidence of leakage.				
Test Date: 20-9-2023				



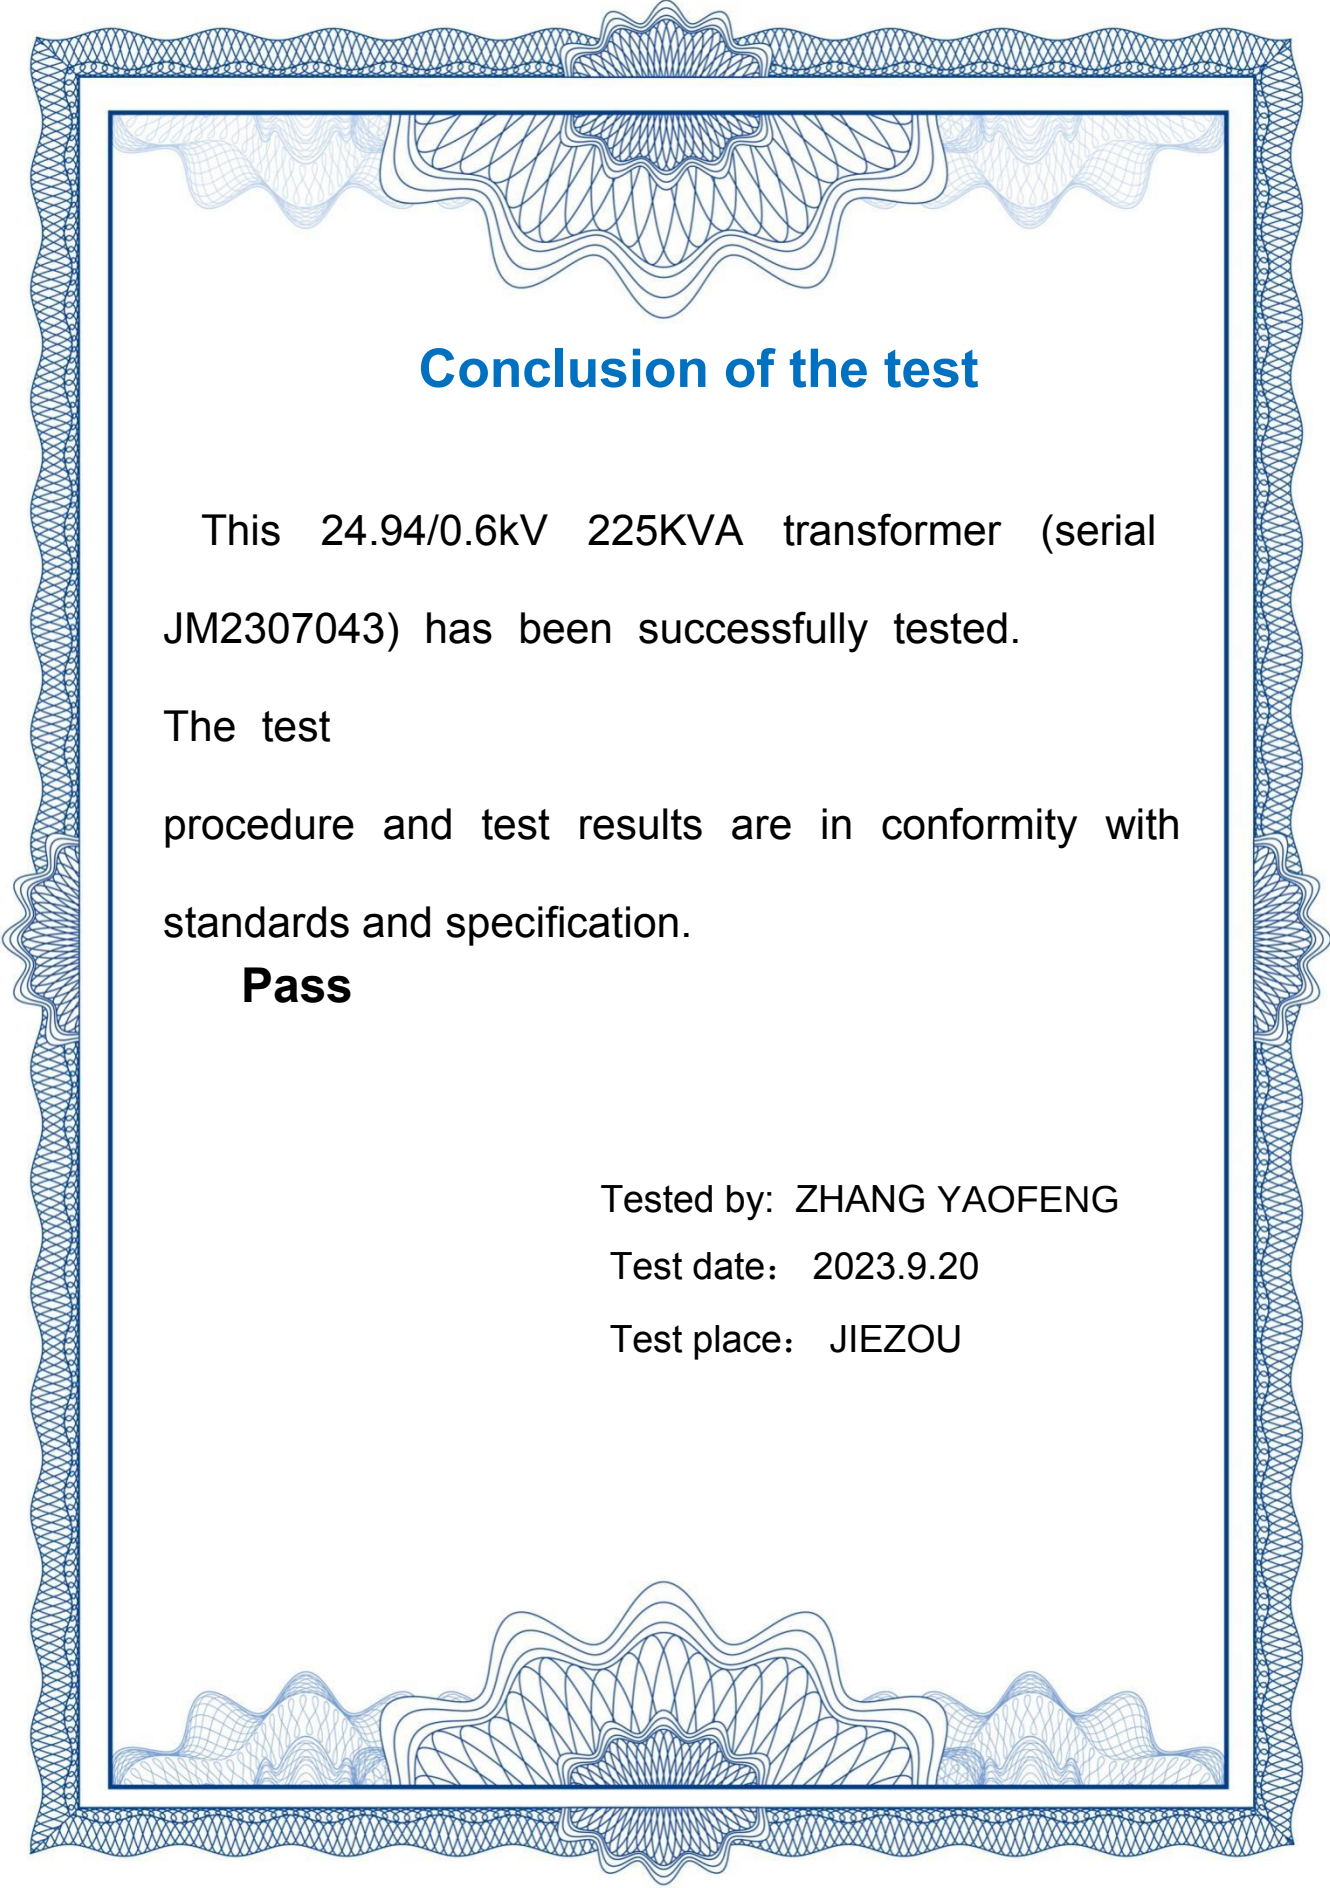

Conclusion of the test

This 24.94/0.6kV 225KVA transformer (serial JM2307043) has been successfully tested.

The test procedure and test results are in conformity with standards and specification.

Pass

Tested by: ZHANG YAOFENG

Test date: 2023.9.20

Test place: JIEZOU
