

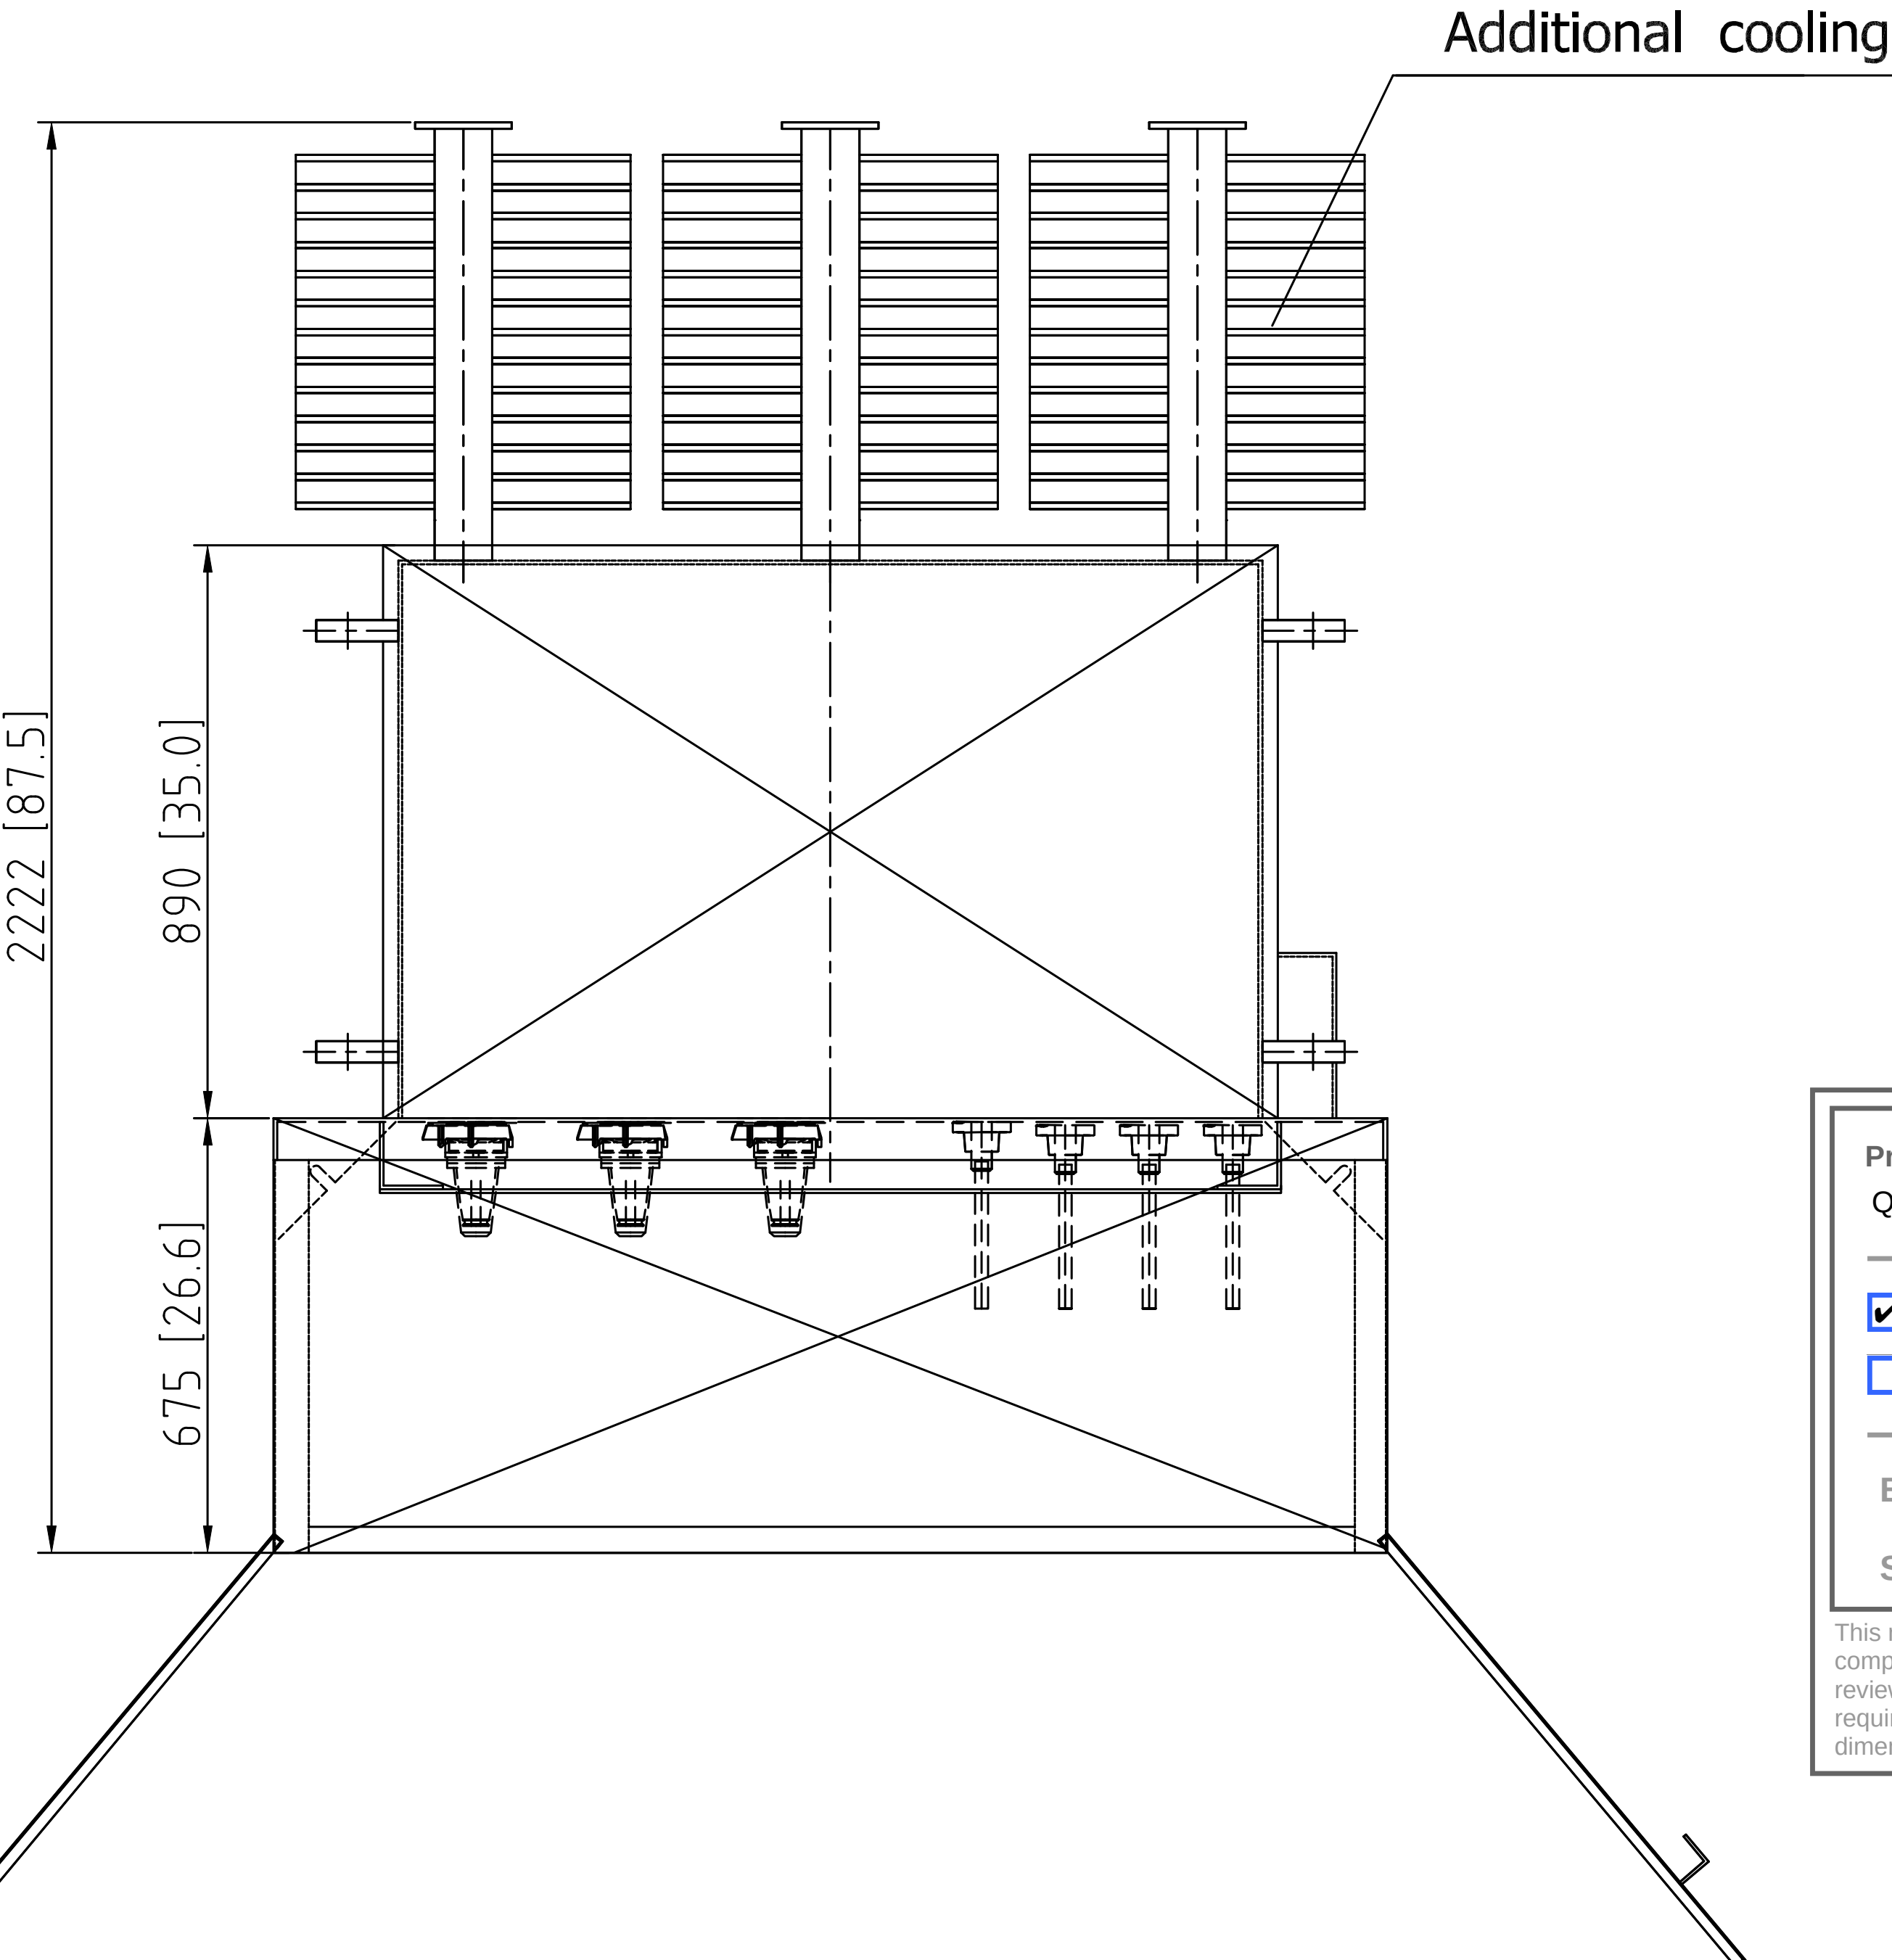
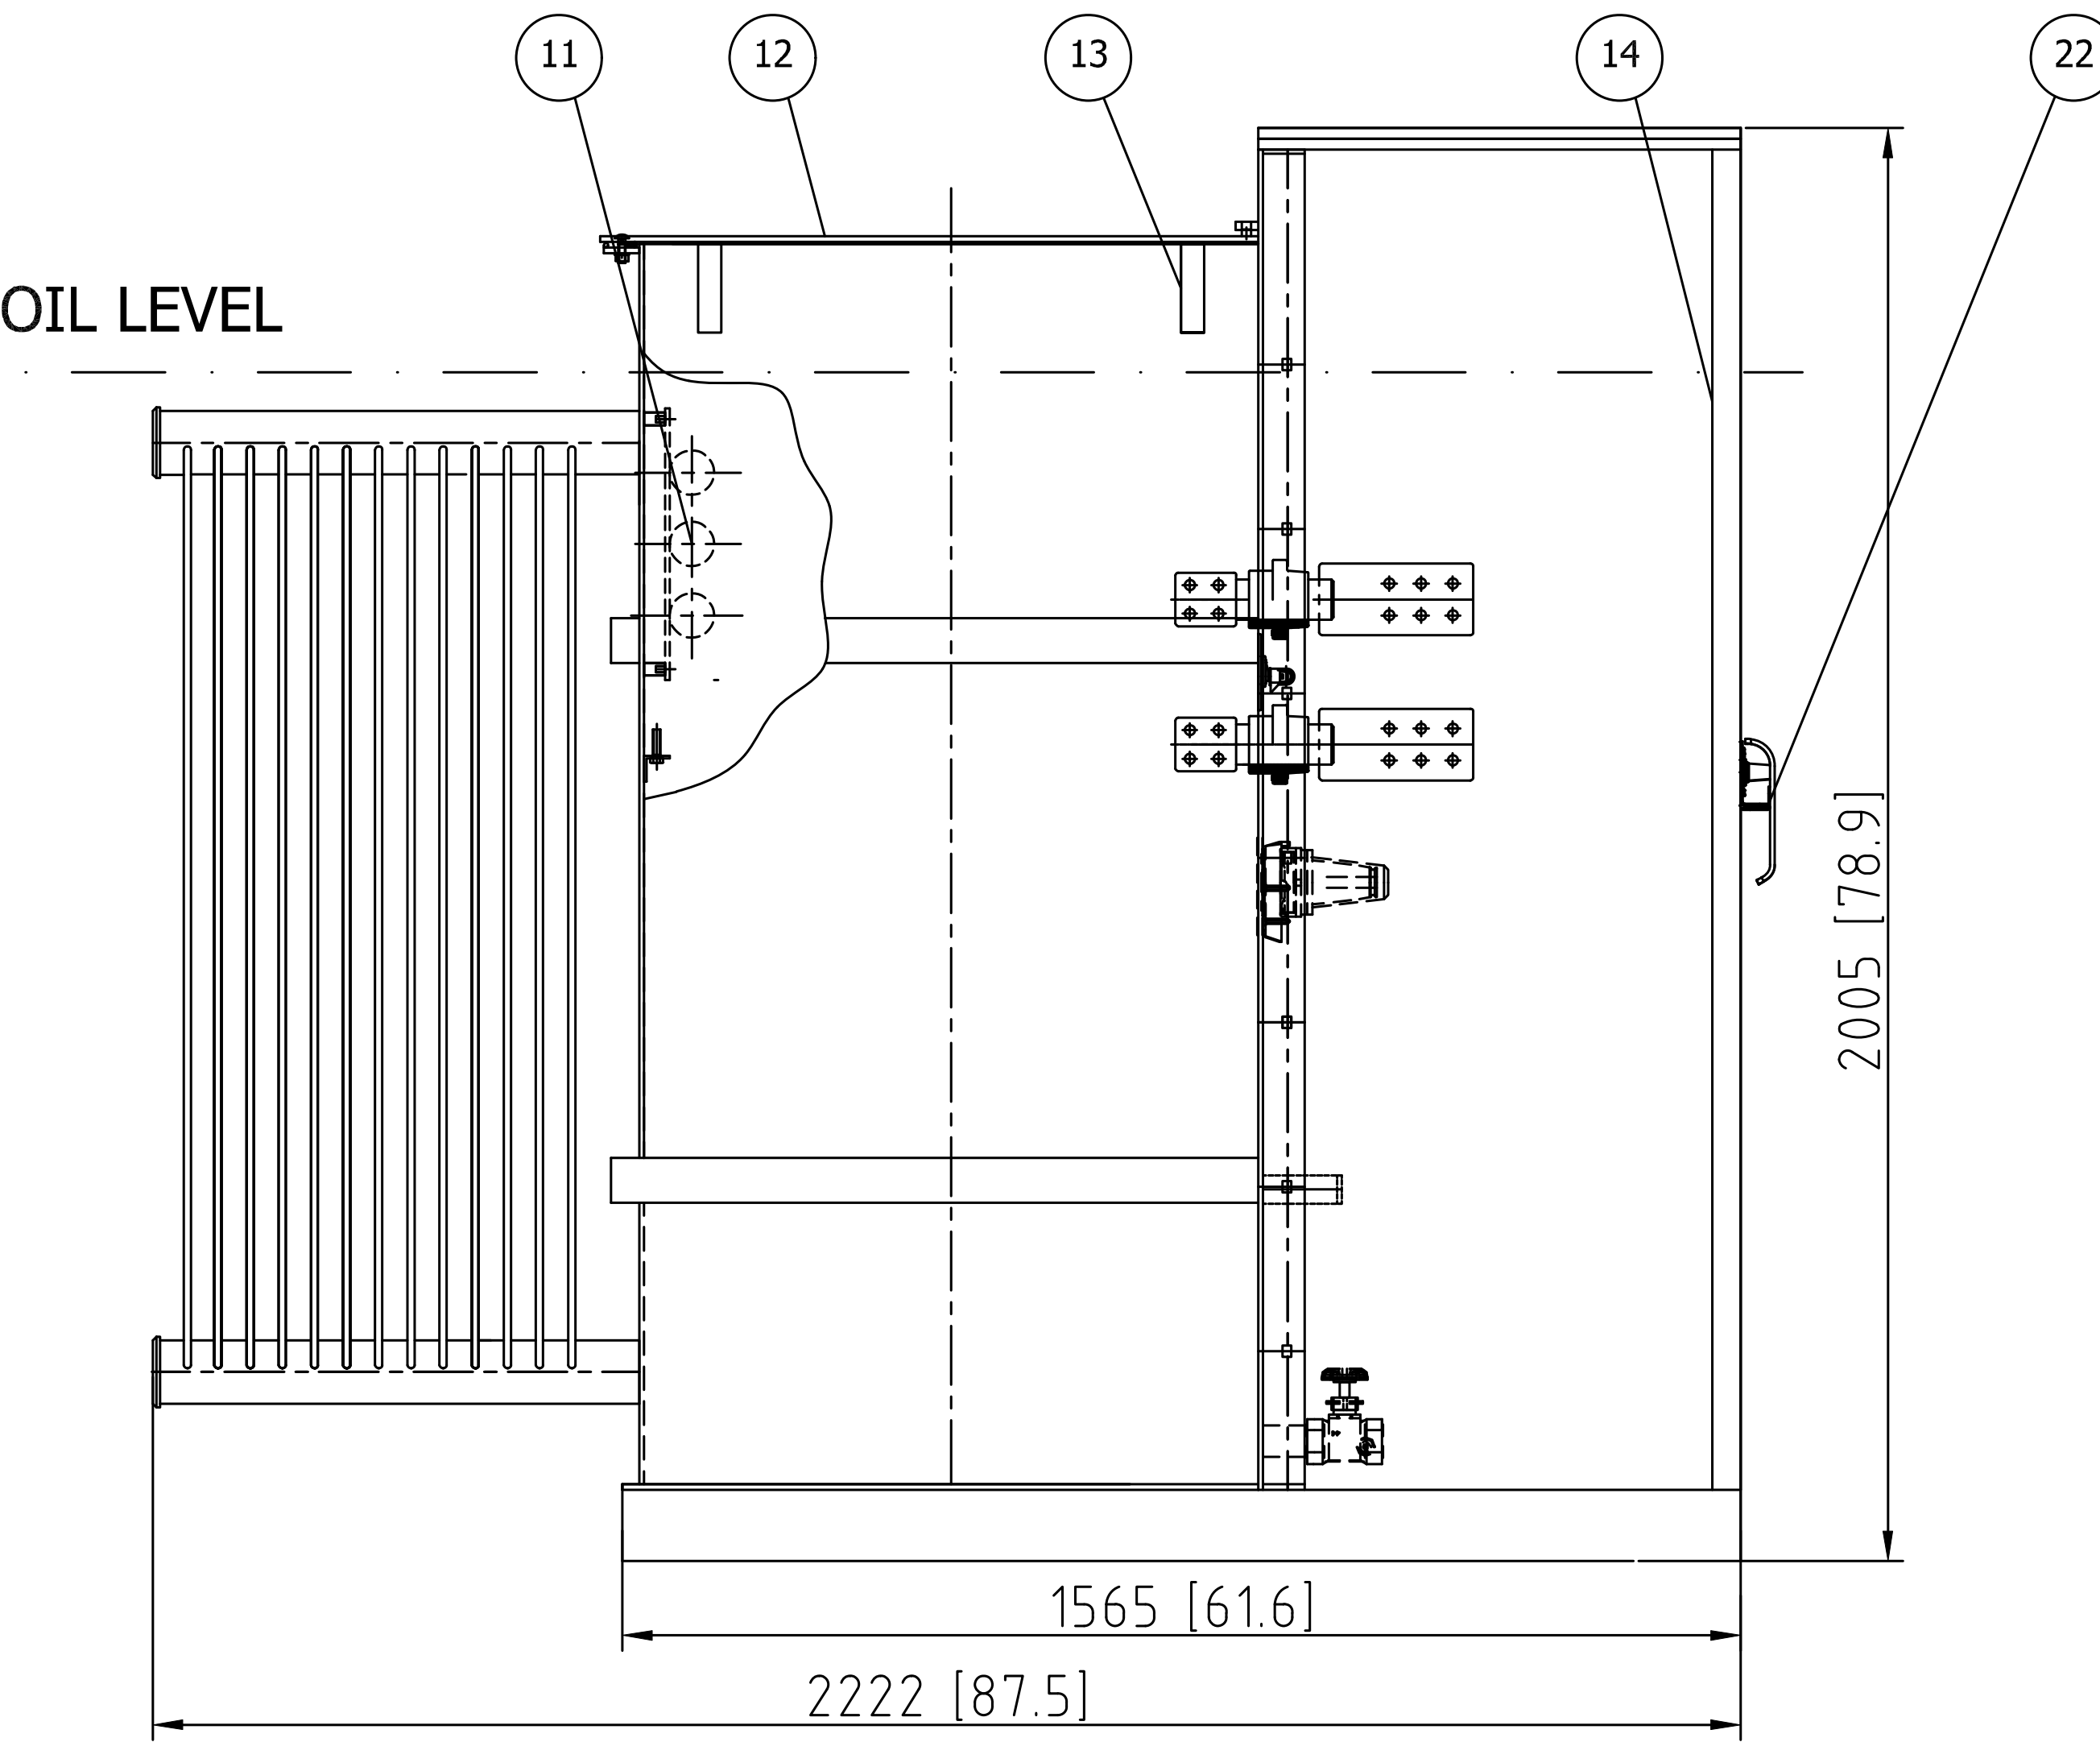
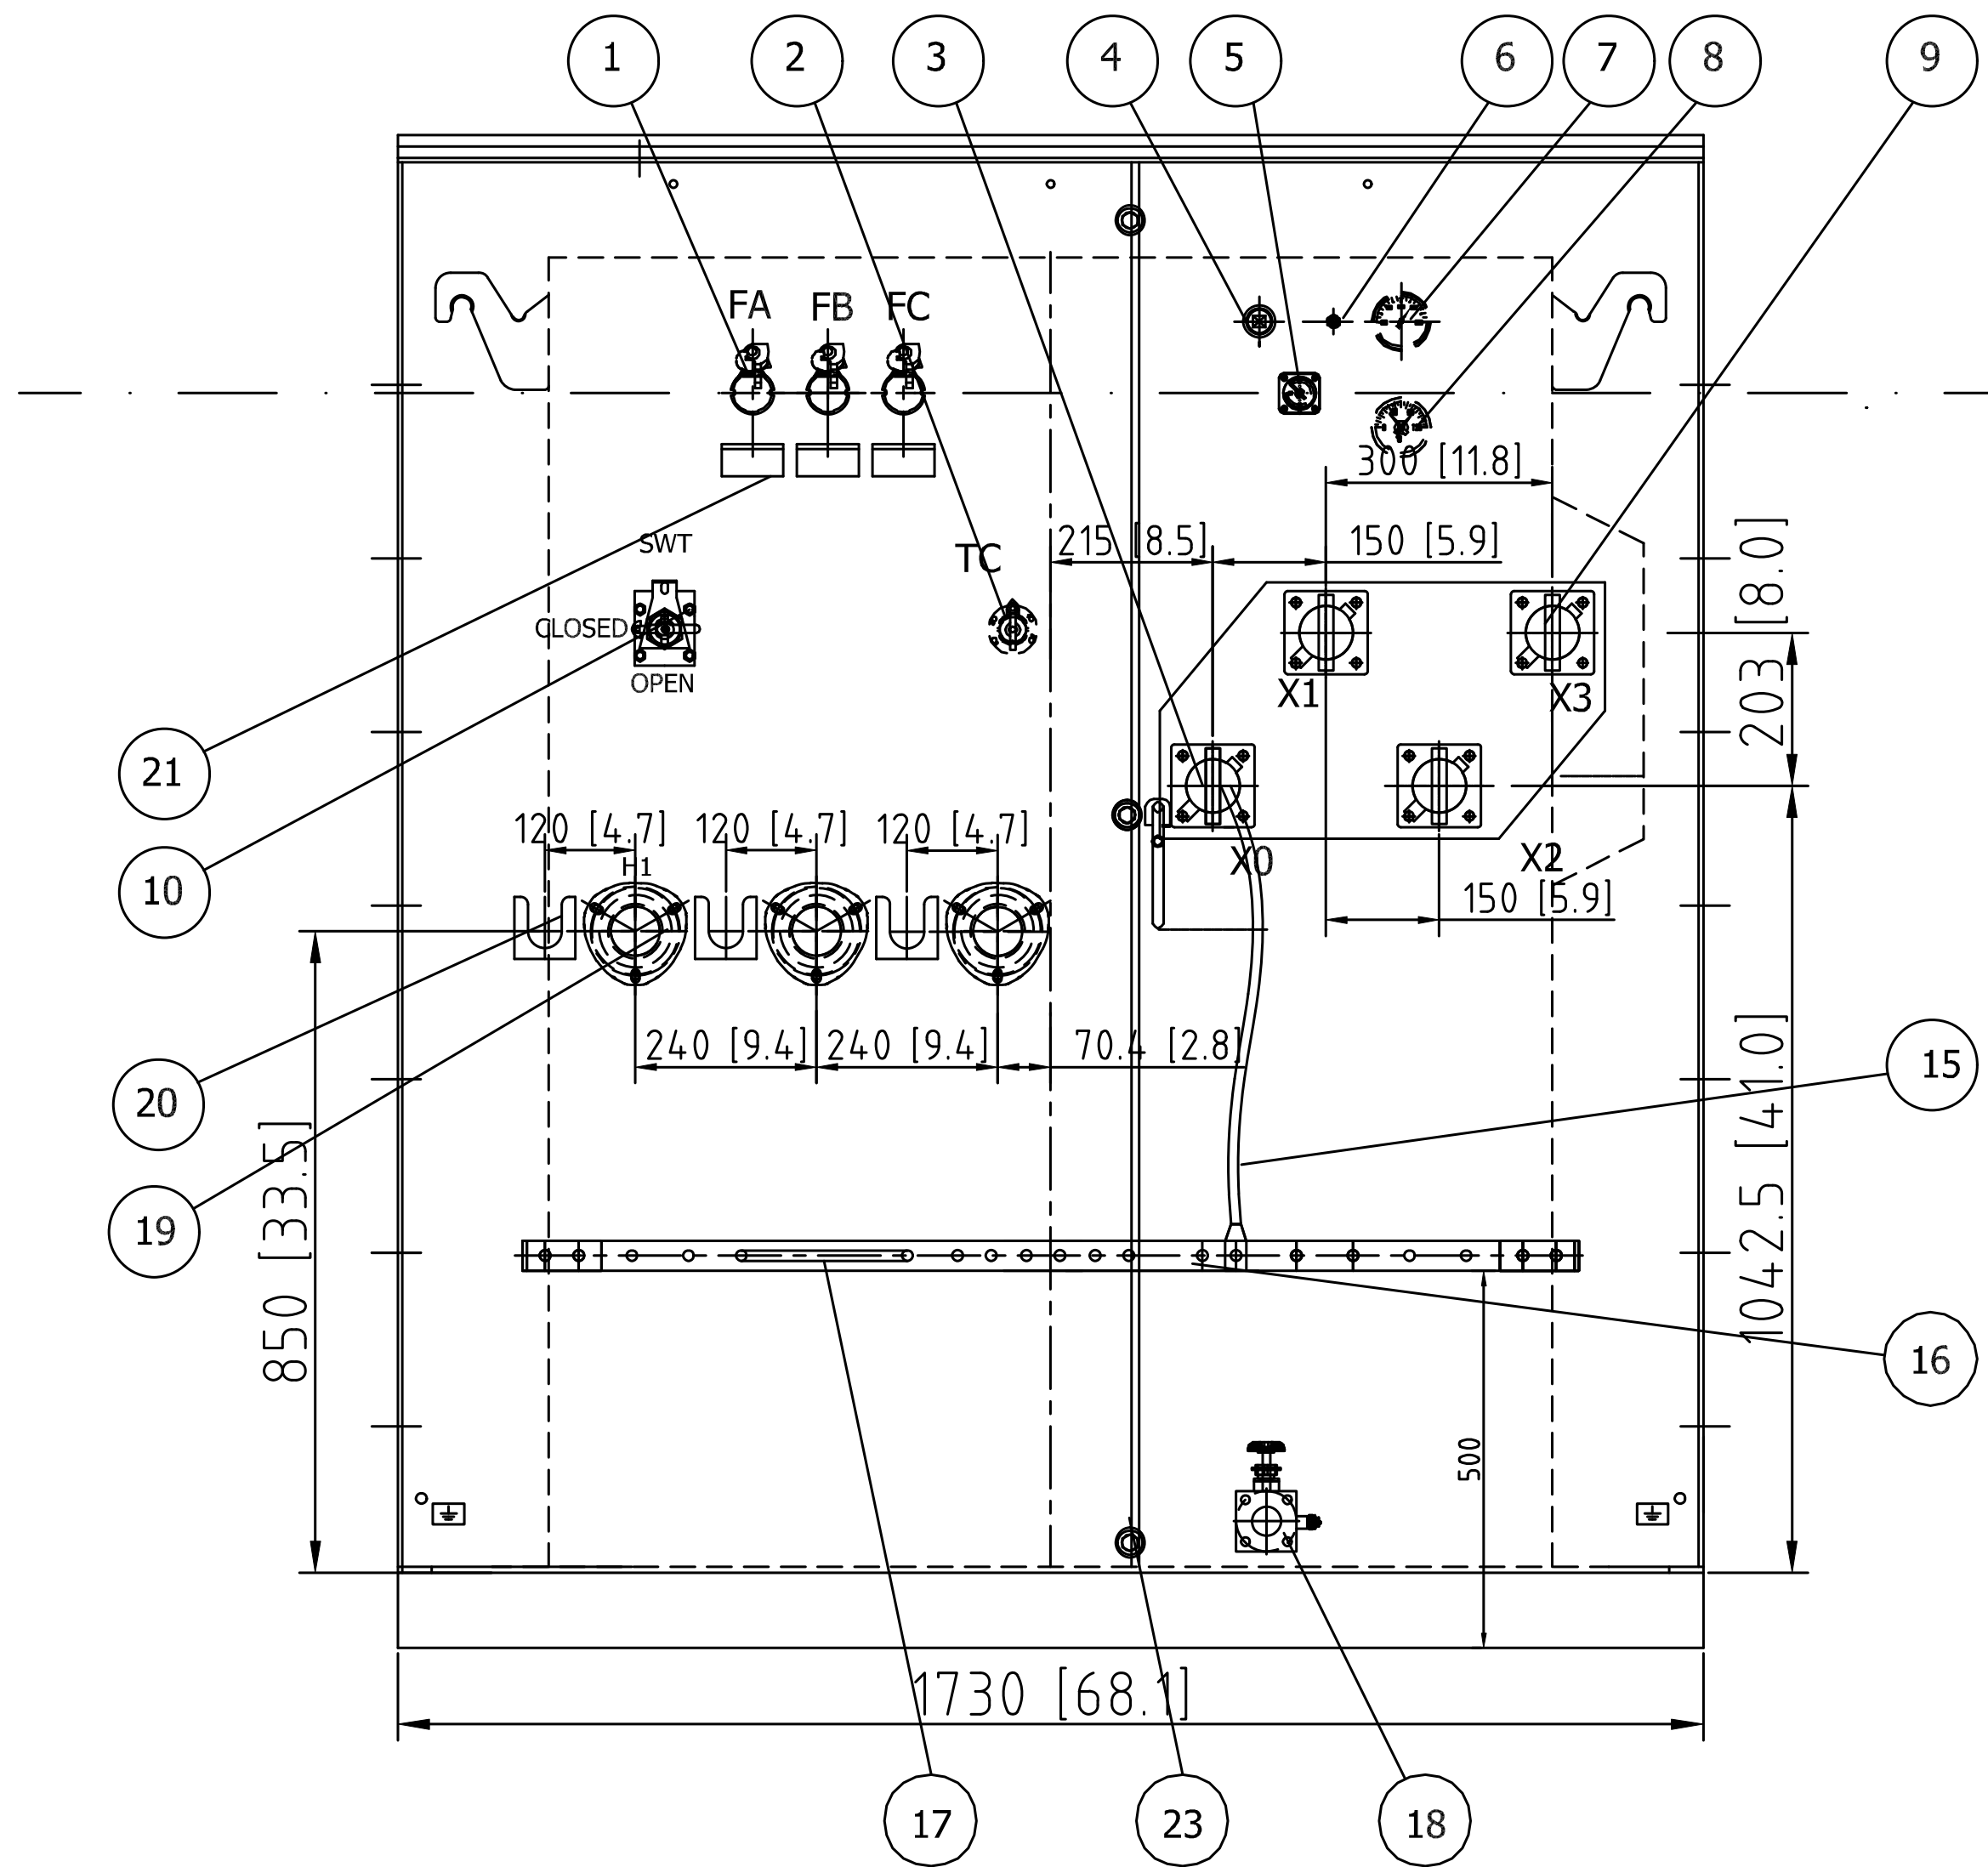


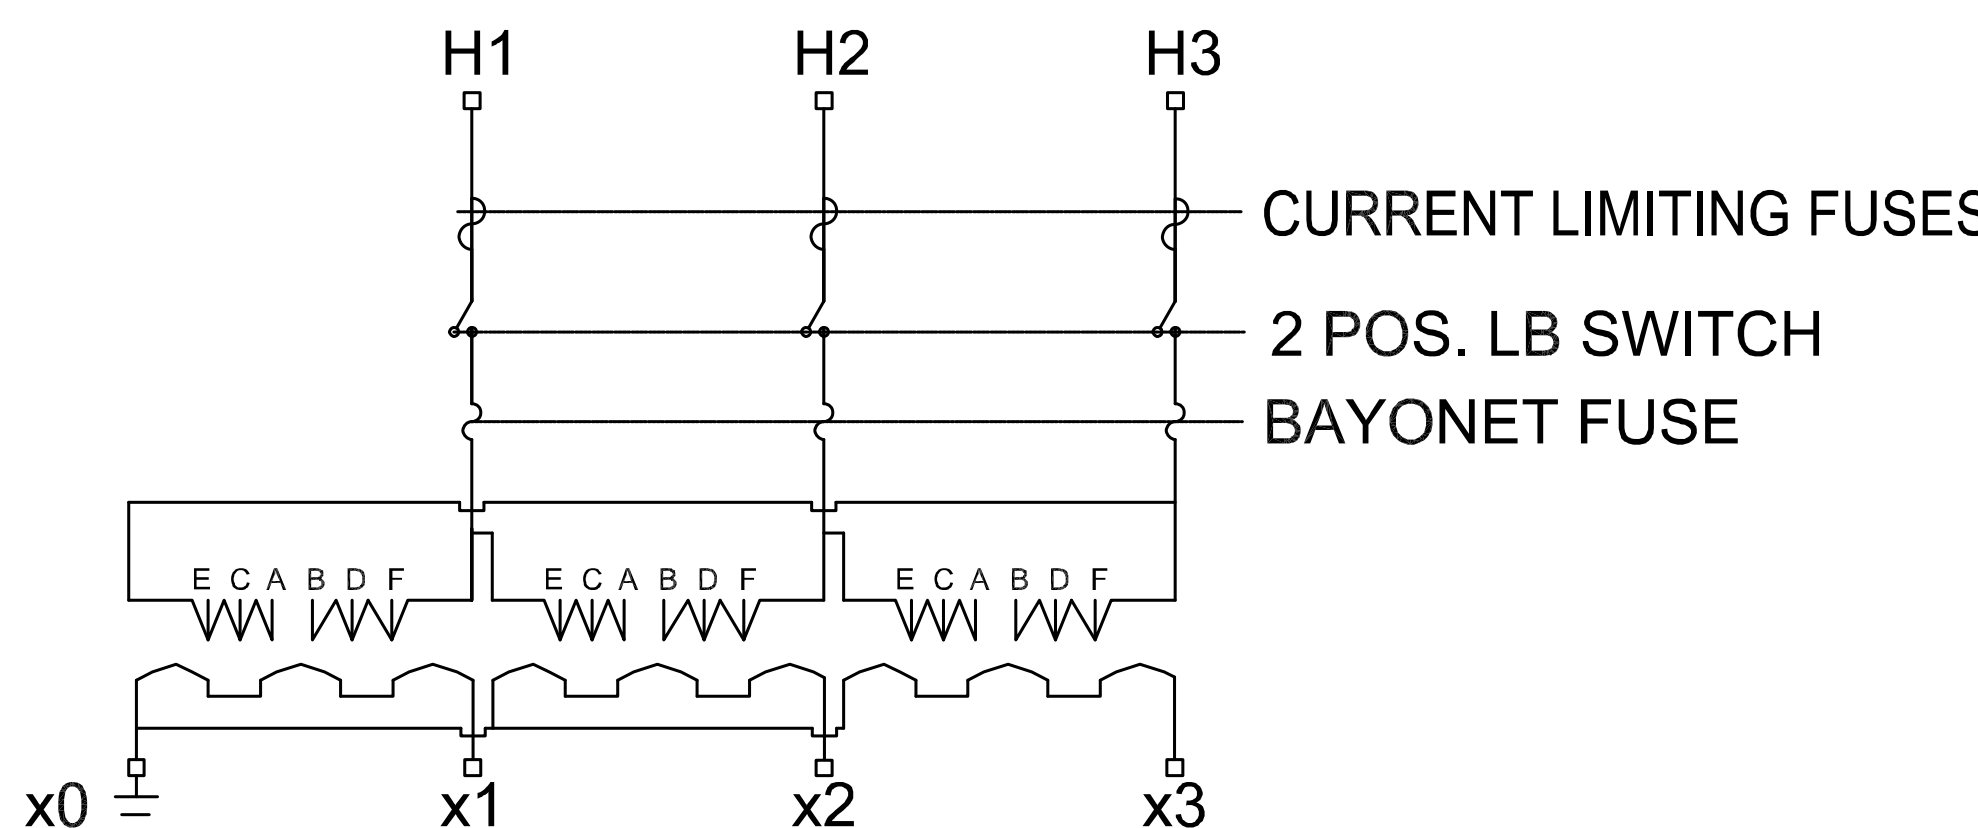

Additional cooling

L.V. TERMINAL

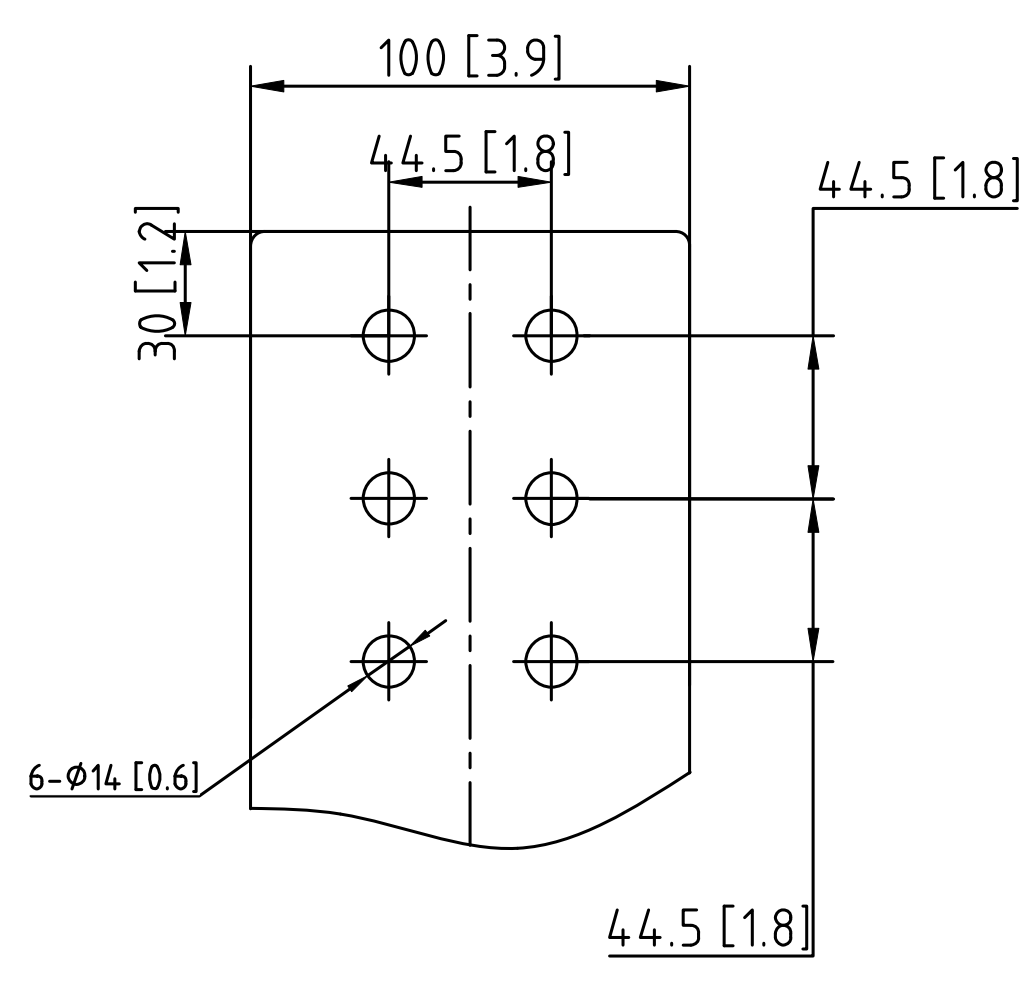

Project Name  
Quik Farm

SitePower  
engineering consultants

☒ APPROVED

☐ REJECTED

☐ REVISE

☐ NOT REVIEWED

BY Mat Bearchell

DATE 4/15/2024

SUBMITTAL#

SPEC 23138

This review is only for general conformance of the project and general compliance. Corrections or comments made on these drawings during this review do not relieve Contractor/Subcontractor from compliance with the requirements of the plans and specifications. Contractor is responsible for all dimensions and fabrication to be confirmed and correlated at the job site

| ITEM             | WEIGHT(LBS) |
|------------------|-------------|
| CORE WEIGHT      | 3460 LBS    |
| TOTAL OIL WEIGHT | 395 GALS    |
| TOTAL WEIGHT     | 9175 LBS    |

| TECHNICAL DATA             |                          |
|----------------------------|--------------------------|
| RATING                     | 1500kVA                  |
| PRIMARY VOLTAGE(V)         | 25000 Delta              |
| SECONDARY VOLTAGE(V)       | 600GrdY/347              |
| FREQUENCY                  | 60Hz                     |
| VECTOR GROUP               | Dyn1                     |
| CONDUCTOR                  | ALUMINUM                 |
| PRIMARY BIL VOLTAGE        | 150kV                    |
| SECONDARY BIL VOLTAGE      | 30kV                     |
| INSULATING OIL             | MINERAL OIL              |
| TEMPERATURE RISE           | 65°C                     |
| LOAD LOSS AT RATED VOLTAGE | 15000 W                  |
| NO LOAD LOSSES             | 2200 W                   |
| IMPEDANCE                  | 5.75%                    |
| ALTITUDE                   | ≤1000m                   |
| COLOR                      | Fortis Green             |
| CORE FORM                  | THREE-PHASE THREE-COLUMN |

| PARTS LIST |                                         |     |
|------------|-----------------------------------------|-----|
| ITEM       | DESCRIPTION                             | QTY |
| 1          | BAYONET FUSE(4000380C14CB)              | 3   |
| 2          | TAP CHANGER(WSLII3 63/35-6×5)           | 1   |
| 3          | L.V BUSHING(FTG1-1/3150,6-HOLE BIL30kV) | 4   |
| 4          | FILL PLUG                               | 1   |
| 5          | OIL LEVEL GAUGE(UHZ-01)                 | 1   |
| 6          | PRESSURE RELIEF VALVE                   | 1   |
| 7          | VACUUM PRESSURE GAUGE (Y100)            | 1   |
| 8          | OIL TEMPERATURE INDICATOR(WSS-401)      | 1   |
| 9          | NAME PLATE                              | 1   |
| 10         | TWO POSITION LB SWITCH                  | 1   |
| 11         | ELSP FUSE(CBUC38140D100)                | 3   |
| 12         | TANK COVER                              | 1   |
| 13         | LIFTING LUG                             | 4   |
| 14         | HINGED DOOR                             | 2   |
| 15         | GROUND STRAP COPPER                     | 1   |
| 16         | GROUND TERMINAL                         | 1   |
| 17         | CEA GROUND BRACKET                      | 1   |
| 18         | 1"DRAIN VALVE WITH 3/8" SAMPLER         | 1   |
| 19         | HV BUSHING WELL (25kV,200A)             | 3   |
| 20         | PAKING STAND BRACKET                    | 3   |
| 21         | DRIP TRAY                               | 1   |
| 22         | DOOR HANDLE                             | 1   |
| 22         | PENTAHEAD BOLT ARRANGEMENT              | 3   |

TYPE  
ZGS-Z-1500/25/0.6

DWG. NAME  
General Assembly Drawing

DRAWN  
Mike

CHECKED  
Jack

CHECKED  
Iris

APPROVED  
Sam

FIRST ANGLE PROJECTION

SCALE  
1

JZP-ZGS1500-240319-001

REV. NO.  
0

CHANGE



